



North Terminal Project Update

April 27, 2017



North Terminal Project


Project Components

Project	Status	NTP Date	Completion Date
Pump Station	Construction	Jan, 2016	July, 2017
NAVAIDs – ASR/LLWAS	FAA Equipment Installation	Feb, 2016	June, 2017
NAVAIDs – RTR Relocation	FAA Equipment Installation	June, 2016	Dec, 2017
NAVAIDs – Cable Loop	Construction	Jan, 2016	Mar, 2017
North Terminal	Construction	Jan, 2016	Feb, 2019
Terminal Access Road*	Contracting	June 2015	Sep, 2018
Hydrant Fueling*	Construction	Feb, 2017	Feb, 2019

* Third party project

North Terminal Program


Project Management – CMAR Invoice Processing Duration

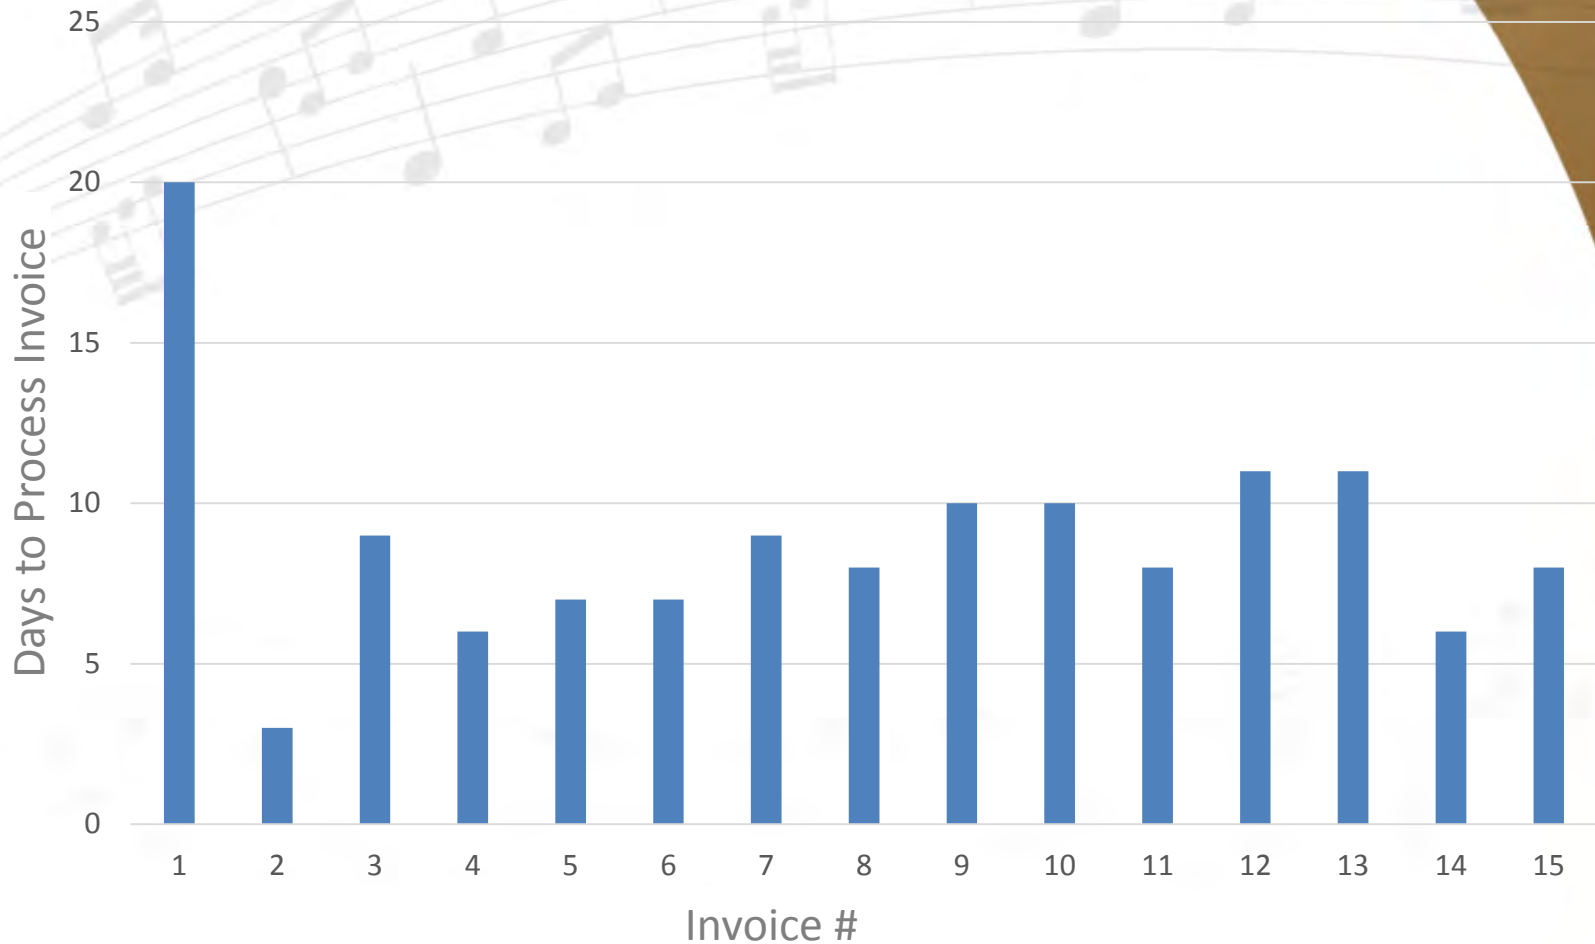

- 20 day process duration requirement met ✓
- 8.9 day average

North Terminal Program

Program Management - Professional Services Invoice Processing Duration

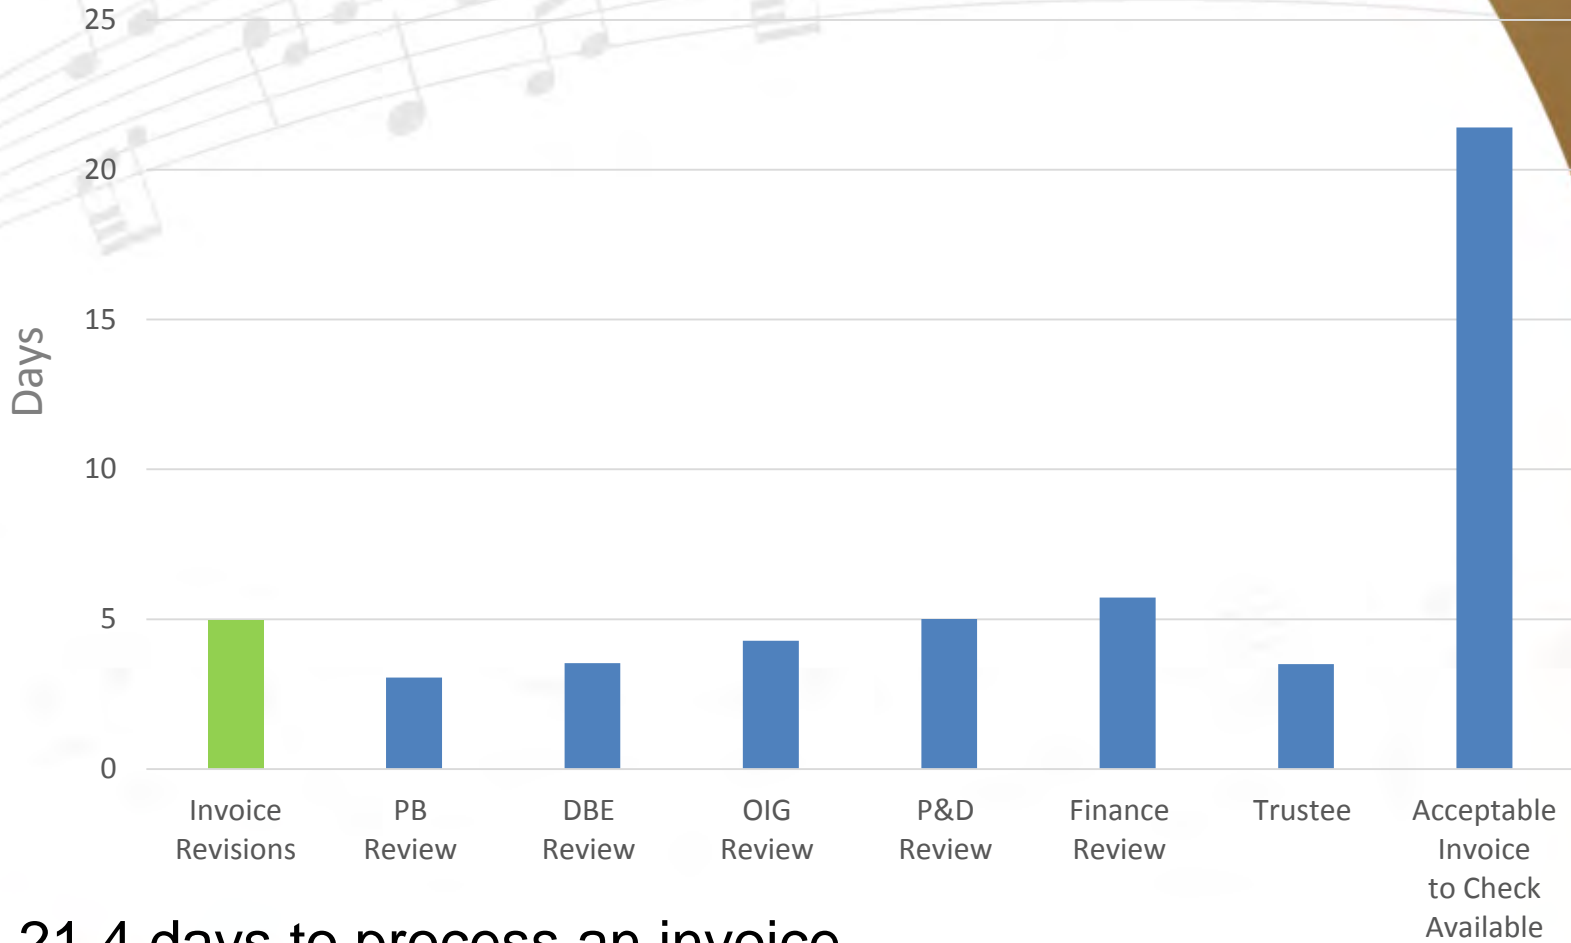

- 21.4 days to process an invoice
- Goal is to process invoices within 30 days ✓

North Terminal Project

April Activities

- North Terminal
 - FAA approval of Second Supplemental EA
 - FAA approval of updated forecast
 - Rating Agency Presentations
 - Steering Committee Meetings – 3rd and 25th
- Enabling Projects
 - Storm Water Pump Station
 - Discharge Piping is 95% complete
 - Pumps, motors and electrical equipment installed
 - NAVAIDs
 - ASR/LLWAS
 - Tower and infrastructure accepted by FAA
 - FAA team mobilized and installing equipment
 - RTR
 - Infrastructure in Place
 - Punch list Items being addressed
 - FAA team mobilized and installing equipment

North Terminal Project

ASR-9 Facility



North Terminal Project

RTR Facility



North Terminal Project

Aerial April 1, 2017

Pump Station



North Terminal Project

Aerial April 1, 2017

CMAR Construction Activities



North Terminal Project

Aerial April 1, 2017 vs BIM Schedule CMAR Construction Activities



Tuesday April 04, 2017





**World Class Airport
for a
World Class City**
