




# North Terminal Project Update

**Board Meeting  
January 28, 2016**



# North Terminal Project

## Project Components

Project	Status	NTP Date	Completion Date
Airfield Lighting Vault	Close Out	Nov 25, 2014	Feb 1, 2016
Test Piles	Final Analysis		
Pump Station	Limited NTP Issued	Jan 20, 2016	July 13, 2017
NAVAIDs – ASR/LLWAS	Limited NTP Issued	Jan 7, 2016	Aug 5, 2016
NAVAIDs – RTR Relocation	Pending NTP	Feb 22, 2016	Sept 19, 2016
NAVAIDs – Cable Loop	Mobilization	Jan 7, 2016	Aug 1, 2016
North Terminal	Mobilization	Jan 7, 2016	Oct 1, 2018
Terminal Access Road*	Design	June 2015	Dec 28, 2016
Hotel *	RFP prepared		Oct 1, 2018
Hydrant Fueling*	Design		
Concessions Program	RFP in development		Oct 1, 2018


\* third party project

# North Terminal Project


## December/January Milestones

- North Terminal
  - CMAR contract awarded for GMP of \$598,979,208.
  - All building permits secured
  - NTP issued
  - Ground breaking held
  - Test Pile program complete
- Enabling Projects
  - Storm Water Pump Station
    - Preconstruction meeting held
    - Limited NTP issued
    - USACE Letter of No Objection received
  - NAVAIDs
    - NTP issued - ASR/LLWAS
    - RA 2189 Executed RTR Location

# North Terminal Project DBE Update

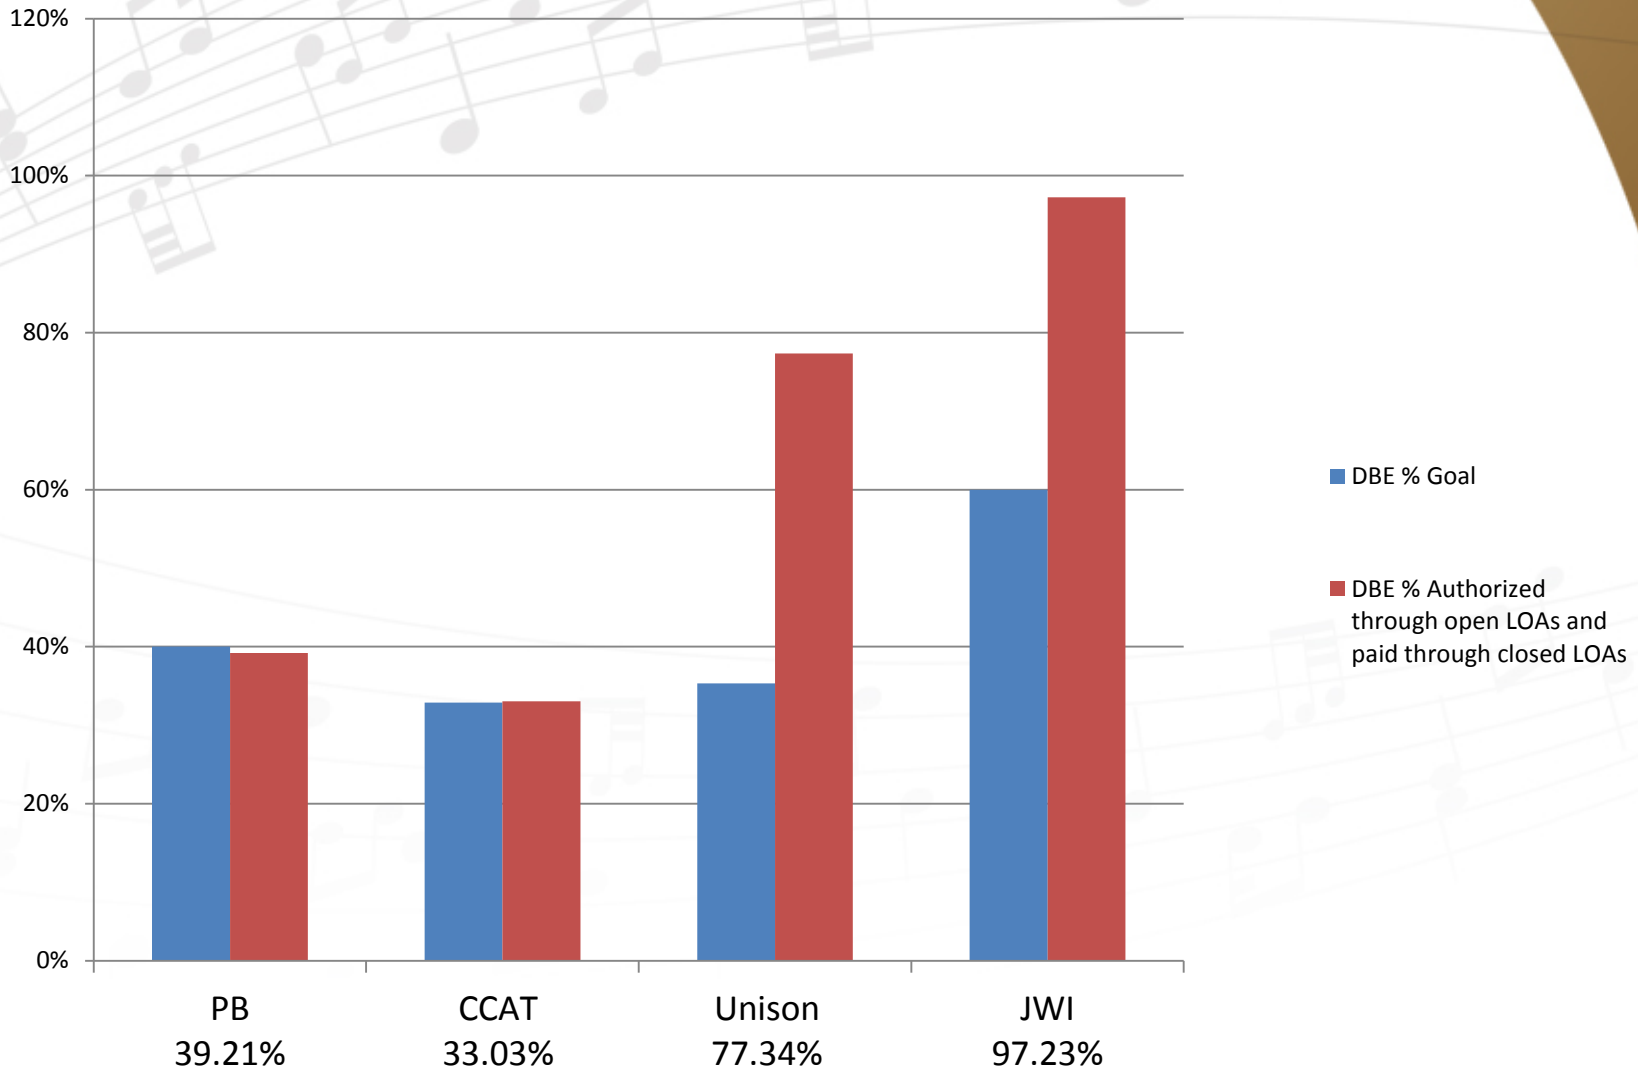

# North Terminal Project Invoice Processing Durations

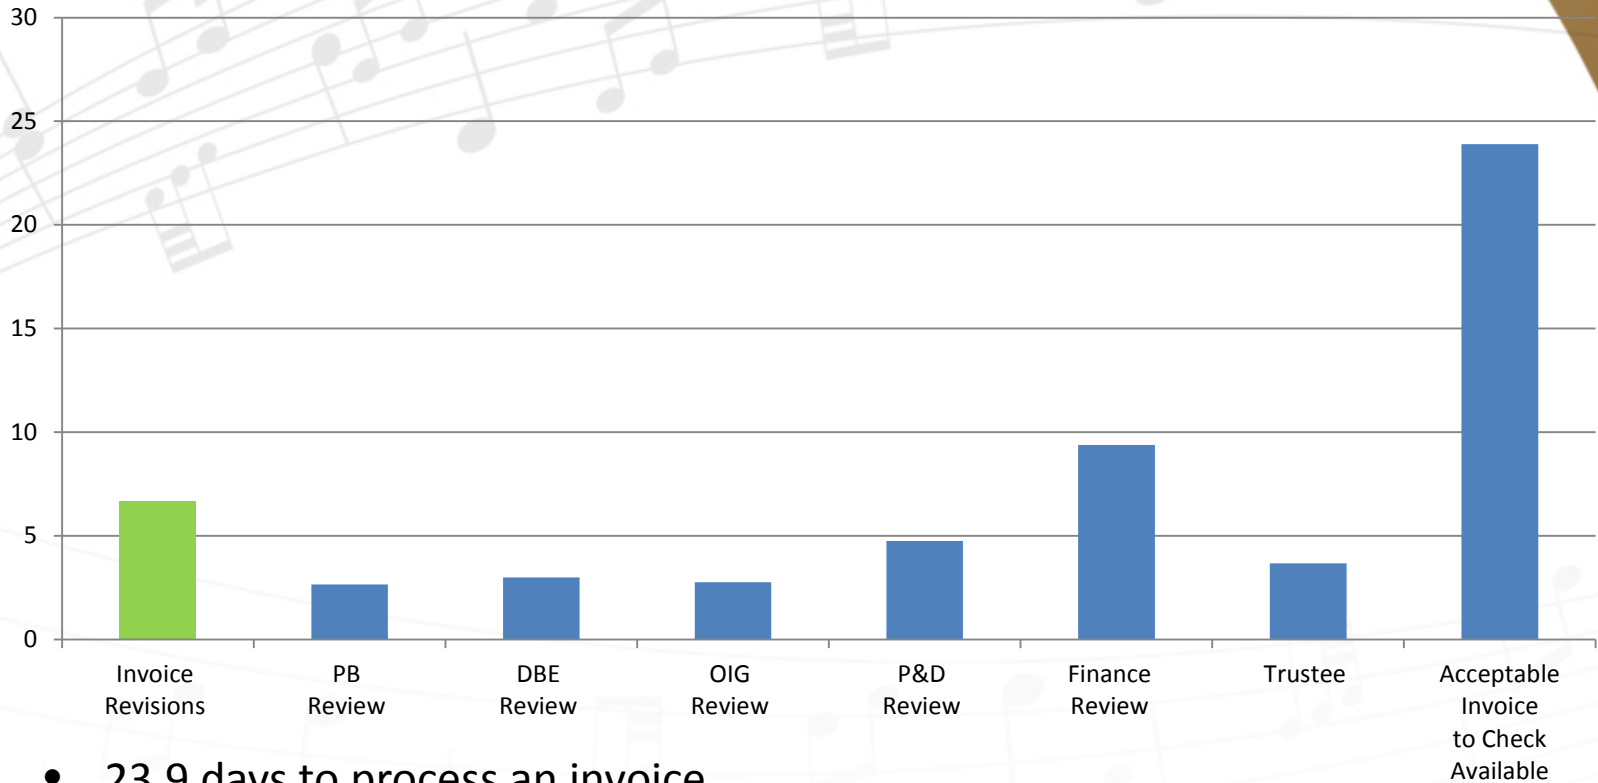

- 23.9 days to process an invoice

# North Terminal Project

- Current Activities
  - Site office complex permits received
  - Office complex site preparation
  - Master schedule development
  - DBE Compliance reviews and submittals
  - Prime Subcontractor Bonds and Insurance
  - City of Kenner Building Inspection coordination
- 3 Week Look Ahead
  - DBE Outreach Meeting planned for 2/3/2016 at Airport Hilton
  - FAA Loop relocation initiated
  - Early Construction Package Submittals Initiated
  - Piling, Curtain Wall, Structural Steel, Reinforcing, Site Surcharge and Wick, Structural Concrete, SWPPP, ETC.
  - Finalize Structure Pile Lengths utilizing Test Pile results
  - Temporary Power and Utilities for Office Complex and Construction Site
  - Contractor Master Schedule
  - DBE Compliance, Initiation of Reporting and LCP Tracker, Davis Bacon and B2G Training
  - Site prep for surcharge/wicks





**World Class Airport  
for a  
World Class City**
