



North Terminal Project Update

March 17, 2016



North Terminal Project

Project Components

Project	Status	NTP Date	Completion Date
Airfield Lighting Vault	Close Out	Nov 25, 2014	Feb 1, 2016
Test Piles	Completed	Aug 31, 2015	Mar 1, 2016
Pump Station	Construction	Jan 29, 2016	July 22, 2017
NAVAIDs – ASR/LLWAS	Construction	Feb 15, 2016	Sept 11, 2016
NAVAIDs – RTR Relocation	Bidding	May 1, 2016	Jan 15, 2017
NAVAIDs – Cable Loop	Construction	Jan 7, 2016	Aug 1, 2016
North Terminal	Construction	Jan 7, 2016	Oct 1, 2018
Terminal Access Road*	Design	June 2015	Dec 28, 2016
Hydrant Fueling*	100% Design in review	TBD by airlines	Oct 1, 2018

* third party project

North Terminal Project

March Milestones

- North Terminal
 - Participated in City of Kenner Community Outreach event on March 1
 - To inform local residents of CMAR's construction plan and proposed access routes
 - Airline Steering Committee Meetings on March 8 and 22
 - Baggage Handling Operations live simulation on February 23
 - To allow airlines to model proposed baggage handling areas to ensure adequate working space
 - CMAR delivered draft construction Schedule
- Enabling Projects
 - Storm Water Pump Station
 - Pilings installed
 - NAVAIDs
 - ASR/LLWAS
 - Pilings installed
 - RTR
 - Bids opened March 11
 - Contract Award is on today's Agenda for Consideration

North Terminal Project

Construction – Pump Station



North Terminal Project

Construction – Pump Station




North Terminal Project

Construction – ASR 9




North Terminal Project Professional Services DBE Update

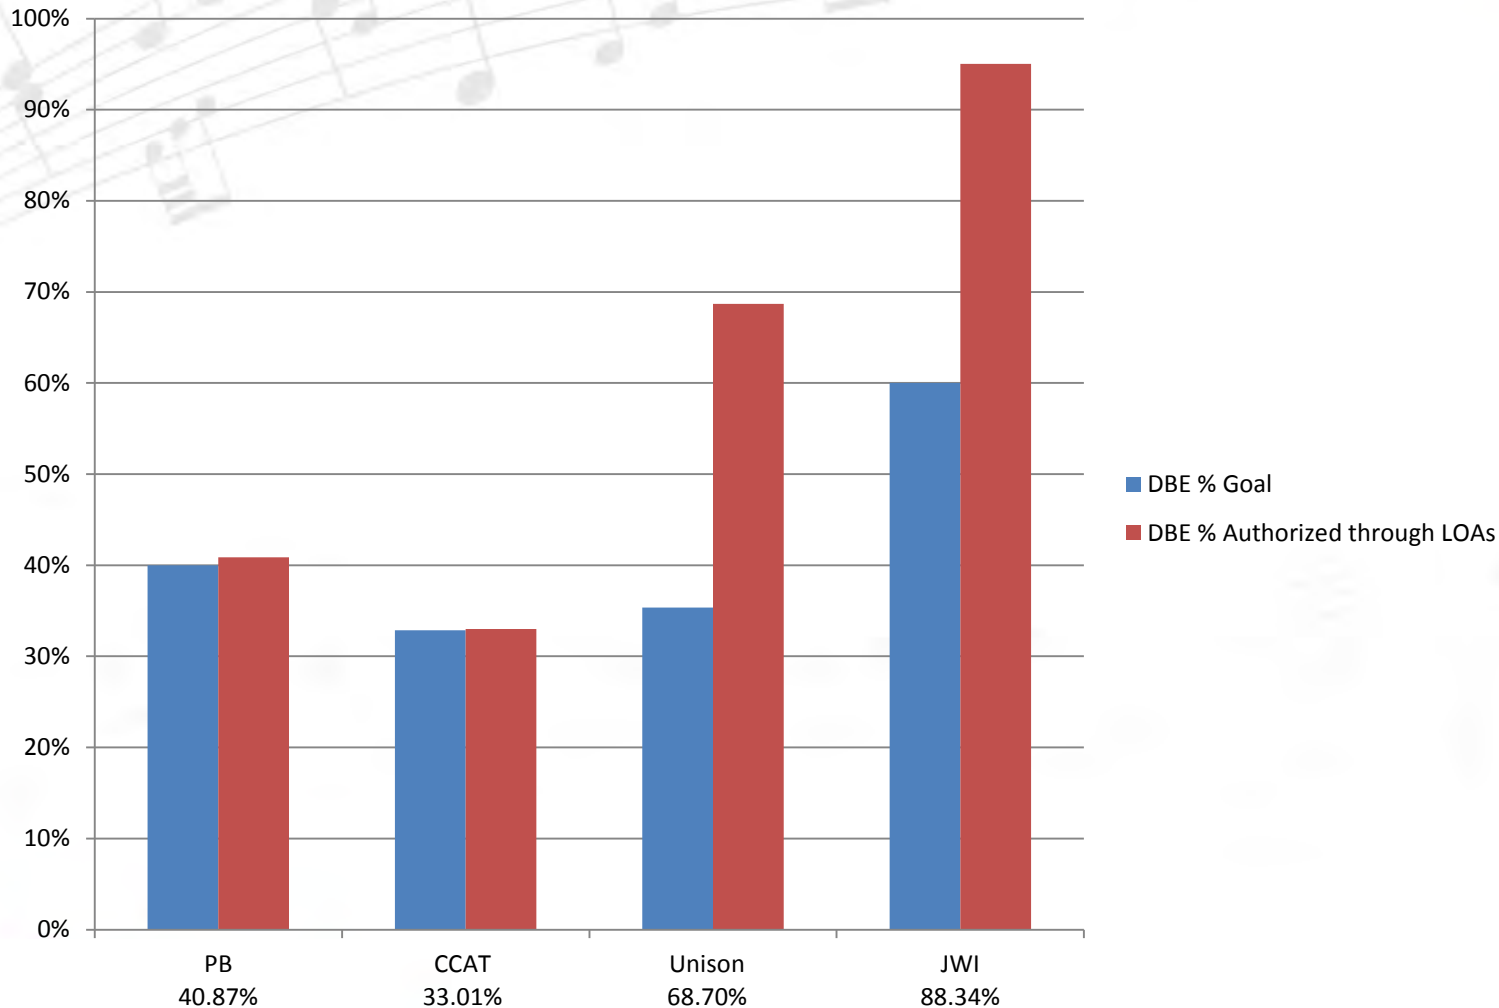

North Terminal Project


Non-CMAR Invoice Processing Durations

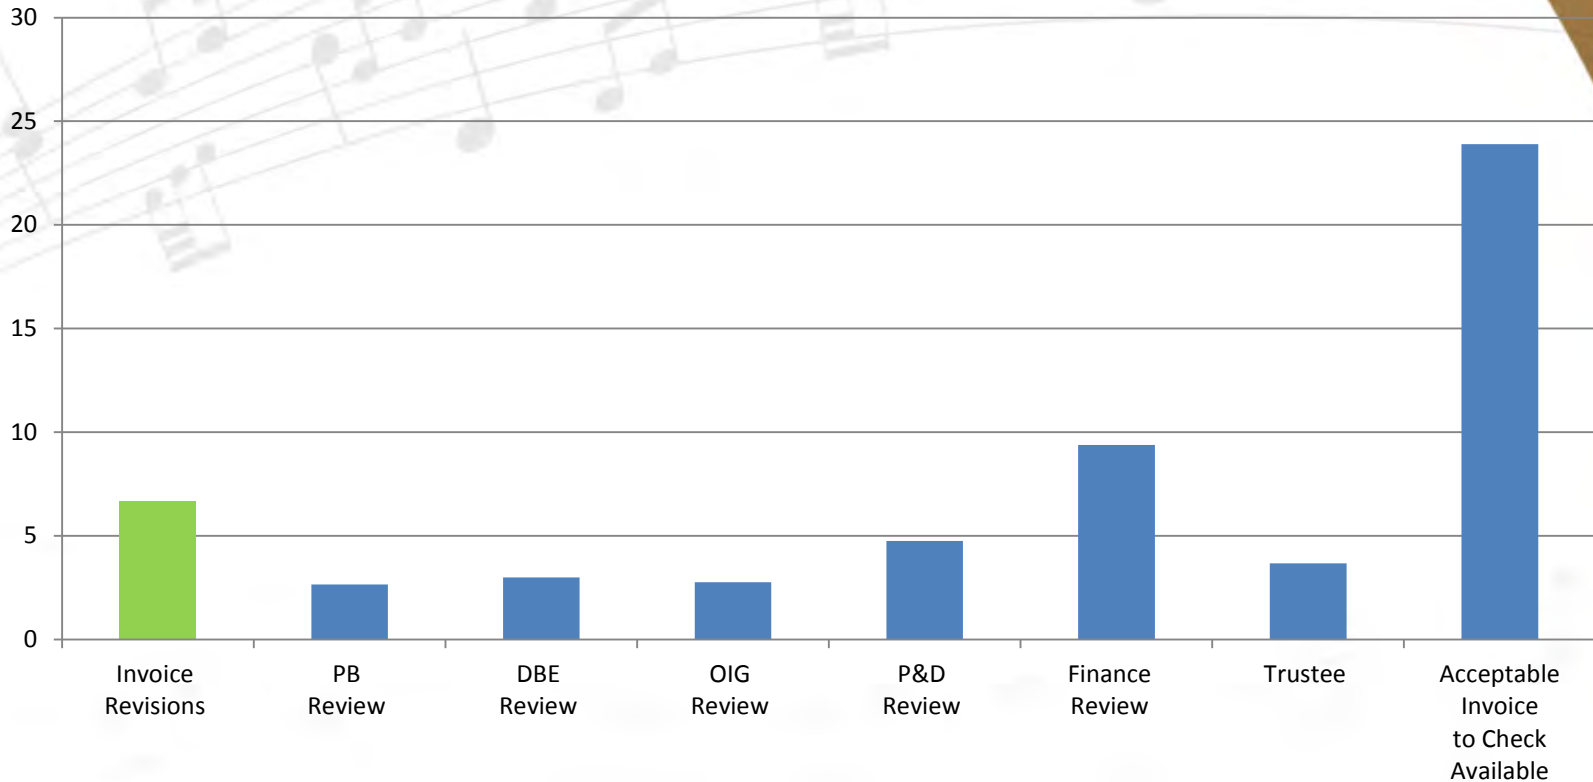

- 24 days to process an invoice
- Goal is to process invoices within 30 days ✓

North Terminal Program

Project Management – CMAR Invoice Processing Duration

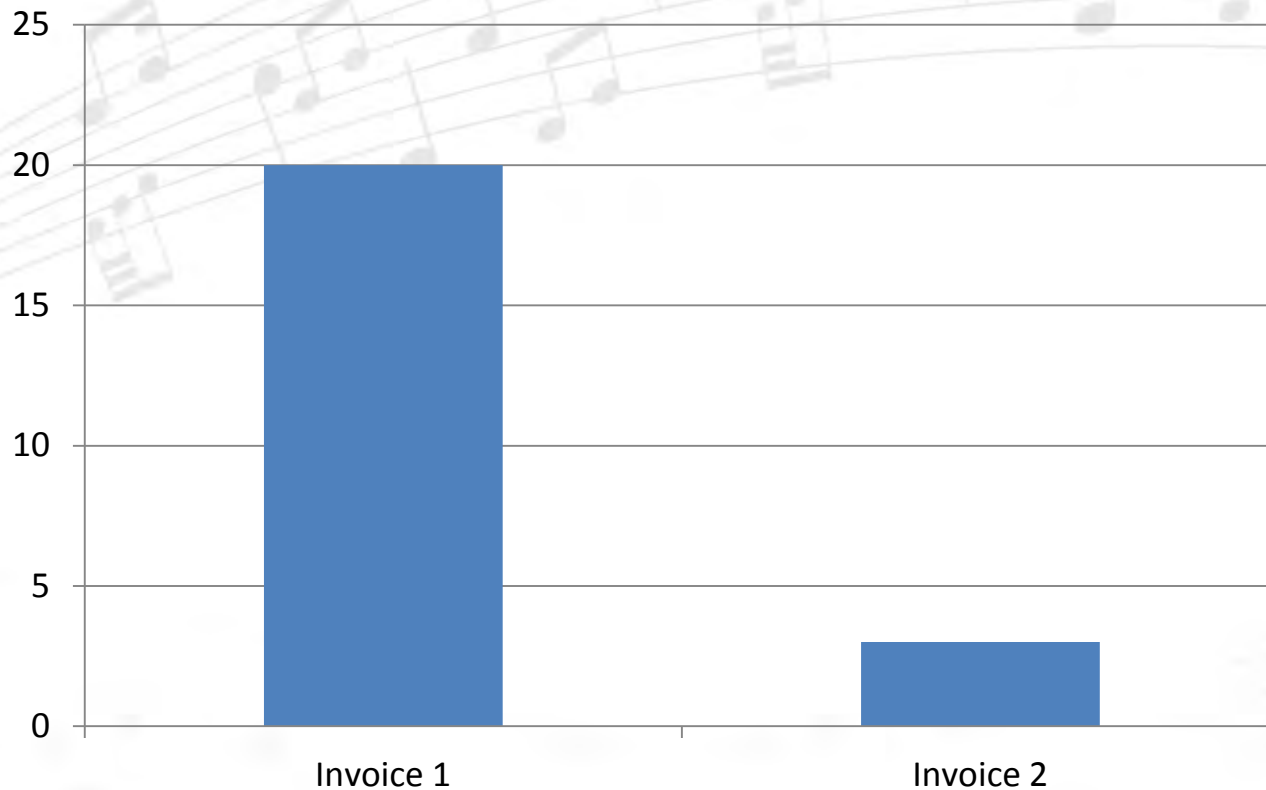

- 20 day process duration requirement met
- Duration reduced 17 days between invoice 1 and 2

North Terminal Project

CMAR Construction Activities

Current Activities

- Office complex site preparation
- Draft Master schedule delivered
- Workforce Development coordination
- DBE Compliance reviews and submittals
- Prime Subcontractor Bonds and Insurance
- RTA coordination

3 Week Look Ahead

- FAA Loop relocation initiated – first phase completed
- Early Construction Package Submittals Initiated
- Piling, Curtain Wall, Structural Steel, Reinforcing, Site Surcharge and Wick, Structural Concrete, SWPPP, ETC.
- Finalize Structural Pile Lengths utilizing Test Pile results
- Temporary Power and Utilities for Office Complex and Construction Site
- DBE Compliance, Initiation of Reporting and LCP Tracker, Davis Bacon and B2G Training
- Site prep for surcharge/wicks

North Terminal Project

Construction – Office Complex Site



North Terminal Project

Construction – FAA Cable Loop



North Terminal Project

Construction – FAA Cable Loop



North Terminal Project

Construction – FAA Cable Loop





**World Class Airport
for a
World Class City**
